



1	Sprint1 Applicati 4.1. Ap 4.2. Sc 4.3. da 4.4 Tra  5.1. User 5.1.1 C Sprint 2	ion Architecture oplication architecture ource code developmentabase Design ack module developmentabase for dispate GUI for Tracks GUI for dispatcher	ent nent and Integration	53 days 7 days 3 days 12 days 6 days 3 days 46 days 10 days 25 days	Mon 1/9/17 Mon 1/9/17 Mon 1/9/17 Mon 1/9/17 Wed 1/18/17 Mon 1/30/17 Wed 1/18/17 Wed 1/18/17	Wed 3/22/17 Tue 1/17/17 Wed 1/11/17 Wed 2/1/17 Wed 2/1/17 Wed 2/1/17 Wed 2/1/17 Wed 3/22/17 Wed 3/1/17	M T W T
3	4.1. Ap 4.2. So 4.3. da 4.4 Tra  5.1. User 5.1.1 ( 5.1.2 (  Sprint 2  5.1.2. so	oplication architectur ource code developmentabase Design ack module development or Interface for dispate GUI for Tracks	ent nent and Integration	3 days 12 days 6 days 3 days 46 days 10 days	Mon 1/9/17 Mon 1/9/17 Wed 1/18/17 Mon 1/30/17 <b>Wed 1/18/17</b> Wed 1/18/17	Wed 1/11/17 Wed 2/1/17 Wed 2/1/17 Wed 2/1/17 Wed 2/1/17 Wed 3/22/17	
4	4.2. So 4.3. da 4.4 Tra 5.1. User 5.1.1 ( 5.1.2 ( Sprint 2 5.1.2. so	ource code developmentabase Design ack module developmentaber Interface for dispate GUI for Tracks GUI for dispatcher	ent nent and Integration	12 days 6 days 3 days 46 days 10 days	Mon 1/9/17 Wed 1/18/17 Mon 1/30/17 Wed 1/18/17 Wed 1/18/17	Wed 2/1/17 Wed 2/1/17 Wed 2/1/17 Wed 3/22/17	
5	4.3. da 4.4 Tra  5.1. User 5.1.1 ( 5.1.2 (  Sprint 2  5.1.2. sou	atabase Design ack module developm Interface for dispate GUI for Tracks GUI for dispatcher	nent and Integration	6 days 3 days 46 days 10 days	Wed 1/18/17 Mon 1/30/17  Wed 1/18/17  Wed 1/18/17	Wed 2/1/17 Wed 2/1/17 Wed 3/22/17	
6	4.4 Tra  5.1. User 5.1.1 ( 5.1.2 (  Sprint 2  5.1.2. so	ack module developm r Interface for dispato GUI for Tracks GUI for dispatcher		3 days <b>46 days</b> 10 days	Mon 1/30/17  Wed 1/18/17  Wed 1/18/17	Wed 2/1/17 Wed 3/22/17	
7	5.1. User 5.1.1 ( 5.1.2 (  Sprint 2  5.1.2. so	r Interface for dispato GUI for Tracks GUI for dispatcher		<b>46 days</b> 10 days	<b>Wed 1/18/17</b> Wed 1/18/17	Wed 3/22/17	
8	5.1.1 ( 5.1.2 ( <b>Sprint 2</b> 5.1.2. so	GUI for Tracks GUI for dispatcher	:her	10 days	Wed 1/18/17		
9	5.1.2 ( <b>Sprint 2</b> 5.1.2. so	GUI for dispatcher		-		Wed 3/1/17	
10	<b>Sprint 2</b> 5.1.2. so	·		25 days			
11 <b>* *</b> 12 <b>* *</b> 13 <b>*</b>	5.1.2. so	uran ando for dispata		•	Wed 1/25/17	Tue 2/28/17	
12 <b>*</b> 13 <b>*</b>		urca cada far dianata	Sprint 2		Tue 2/7/17	Fri 3/24/17	
13 🗸 🖈	Client M	5.1.2. source code for dispatcher		27 days	Tue 2/7/17	Wed 3/15/17	
	CHETT IVI	eeting		1 day	Wed 2/8/17	Wed 2/8/17	
	5.1.3. Un	it Test		1 day	Thu 2/23/17	Thu 2/23/17	
14 🗸 🖈	5.3. Trac	k Module		13 days	Tue 2/7/17	Thu 2/23/17	
18 🗸 🖈	5.2 Train	Module		22 days	Thu 2/23/17	Fri 3/24/17	
19 🗸 🖈	5.2.1. train	5.2.1. Integration of dispatcher, track with single train		6 days	Thu 2/23/17	Thu 3/2/17	
20 🗸 🖈	5.2.2 l	Jnit test for single tra	in	1 day	Fri 3/3/17	Fri 3/3/17	
21 🗸 🖈	5.2.3 9	Source code for multi	ple trains	5 days	Sat 3/4/17	Thu 3/9/17	
22 🗸	5.2.4 I modul	ntegration of dispatches	her, train and track	3 days	Fri 3/10/17	Tue 3/14/17	
23 🗸 🖈		Client Meeting		1 day	Wed 3/15/17	Wed 3/15/17	
24 🗸 🖈	5.2.4.	Unit Test for Train Mo	odule	1 day	Wed 3/15/17	Wed 3/15/17	


0	Task Mode	Task Name	Duration	Start	Finish	Predecessors	23, '16 M T W T F
<b>✓</b>	*	5.4. Integration	2 days	Thu 3/16/17	Fri 3/17/17		
	*	Sprint 3	11 days	Mon 3/27/17	Fri 4/7/17		
<b>✓</b>	*	6. Testing	8 days	Mon 3/27/17	Tue 4/4/17		
<b>✓</b>	-5	6.1. Test Analysis reports are checked	1 day	Mon 3/27/17	Mon 3/27/17		
<b>✓</b>	-5	6.2. Test Plans	1 day	Tue 3/28/17	Tue 3/28/17	28	
<b>✓</b>	-	6.3. Integration Test	1 day	Wed 3/29/17	Wed 3/29/17	29	
<b>✓</b>	-5	6.4. Systems Testing	2 days	Thu 3/30/17	Fri 3/31/17	30	
<b>✓</b>	-3	6.5. User Acceptance Test	1 day	Sat 4/1/17	Sat 4/1/17	31	
<b>✓</b>	-5	6.6. Report Results	2 days	Mon 4/3/17	Tue 4/4/17	32	
	*	7. Deployment	6 days	Sun 4/2/17	Fri 4/7/17		
<b>✓</b>	-5	7.1. Staging	1 day	Wed 4/5/17	Wed 4/5/17	33	
<b></b>	-5	7.2. Preparing all documents	3 days	Thu 4/6/17	Mon 4/10/17	35	
	-5	7.3. Documentation	9 days	Tue 4/11/17	Fri 4/21/17	36	
	イングングング	<ul> <li>Mode</li> <li>✓</li> <li>✓<td><ul> <li>Mode</li> <li>★ 5.4. Integration</li> <li>★ Sprint 3</li> <li>★ 6. Testing</li> <li>★ 6.1. Test Analysis reports are checked</li> <li>★ 6.2. Test Plans</li> <li>★ 6.3. Integration Test</li> <li>★ 6.4. Systems Testing</li> <li>★ 6.5. User Acceptance Test</li> <li>★ 6.6. Report Results</li> <li>★ 7. Deployment</li> <li>★ 7.1. Staging</li> <li>▼ 7.2. Preparing all documents</li> </ul></td><td>Mode5.4. Integration2 daysSprint 311 days6. Testing8 days6.1. Test Analysis reports are checked1 day6.2. Test Plans1 day6.3. Integration Test1 day6.4. Systems Testing2 days6.5. User Acceptance Test1 day7. Deployment6 days7.1. Staging1 day7.2. Preparing all documents3 days</td><td>Mode       5.4. Integration       2 days       Thu 3/16/17         Sprint 3       11 days       Mon 3/27/17         ★       6. Testing       8 days       Mon 3/27/17         ★       6.1. Test Analysis reports are checked       1 day       Mon 3/27/17         ★       6.2. Test Plans       1 day       Tue 3/28/17         ★       6.3. Integration Test       1 day       Wed 3/29/17         ★       6.4. Systems Testing       2 days       Thu 3/30/17         ★       6.5. User Acceptance Test       1 day       Sat 4/1/17         ★       7. Deployment       6 days       Sun 4/2/17         ★       7.1. Staging       1 day       Wed 4/5/17         ★       7.2. Preparing all documents       3 days       Thu 4/6/17</td><td>Mode       2 days       Thu 3/16/17       Fri 3/17/17         Sprint 3       11 days       Mon 3/27/17       Fri 4/7/17         Fri 4/7/17       6. Testing       8 days       Mon 3/27/17       Tue 4/4/17         Mon 3/27/17       Tue 4/4/17       Mon 3/27/17       Mon 3/27/17       Mon 3/27/17         Mon 3/27/17       Tue 4/4/17       Mod 3/29/17       Mod 3/29/17       Wed 3/28/17       Wed 3/28/17       Wed 3/28/17       Wed 3/28/17       Wed 3/29/17       Wed 3/29/17       Wed 3/29/17       Wed 3/29/17       Fri 3/31/17       Sat 4/1/17       Fri 4/7/17       Mon 4/2/17       Fri 4/7/17       Mon 4/2/17       Fri 4/7/17       Mon 4/10/17       Mon 4/10/</td><td>Mode       5.4. Integration       2 days       Thu 3/16/17       Fri 3/17/17         Sprint 3       11 days       Mon 3/27/17       Fri 4/7/17         ★       6. Testing       8 days       Mon 3/27/17       Tue 4/4/17         ★       6.1. Test Analysis reports are checked       1 day       Mon 3/27/17       Mon 3/27/17         ★       6.2. Test Plans       1 day       Tue 3/28/17       Tue 3/28/17       28         ★       6.3. Integration Test       1 day       Wed 3/29/17       Wed 3/29/17       29         ★       6.4. Systems Testing       2 days       Thu 3/30/17       Fri 3/31/17       30         ★       6.5. User Acceptance Test       1 day       Sat 4/1/17       Sat 4/1/17       31         ★       7. Deployment       6 days       Sun 4/2/17       Fri 4/7/17         ★       7.1. Staging       1 day       Wed 4/5/17       Wed 4/5/17       33         Ⅲ       7.2. Preparing all documents       3 days       Thu 4/6/17       Mon 4/10/17       35</td></li></ul>	<ul> <li>Mode</li> <li>★ 5.4. Integration</li> <li>★ Sprint 3</li> <li>★ 6. Testing</li> <li>★ 6.1. Test Analysis reports are checked</li> <li>★ 6.2. Test Plans</li> <li>★ 6.3. Integration Test</li> <li>★ 6.4. Systems Testing</li> <li>★ 6.5. User Acceptance Test</li> <li>★ 6.6. Report Results</li> <li>★ 7. Deployment</li> <li>★ 7.1. Staging</li> <li>▼ 7.2. Preparing all documents</li> </ul>	Mode5.4. Integration2 daysSprint 311 days6. Testing8 days6.1. Test Analysis reports are checked1 day6.2. Test Plans1 day6.3. Integration Test1 day6.4. Systems Testing2 days6.5. User Acceptance Test1 day7. Deployment6 days7.1. Staging1 day7.2. Preparing all documents3 days	Mode       5.4. Integration       2 days       Thu 3/16/17         Sprint 3       11 days       Mon 3/27/17         ★       6. Testing       8 days       Mon 3/27/17         ★       6.1. Test Analysis reports are checked       1 day       Mon 3/27/17         ★       6.2. Test Plans       1 day       Tue 3/28/17         ★       6.3. Integration Test       1 day       Wed 3/29/17         ★       6.4. Systems Testing       2 days       Thu 3/30/17         ★       6.5. User Acceptance Test       1 day       Sat 4/1/17         ★       7. Deployment       6 days       Sun 4/2/17         ★       7.1. Staging       1 day       Wed 4/5/17         ★       7.2. Preparing all documents       3 days       Thu 4/6/17	Mode       2 days       Thu 3/16/17       Fri 3/17/17         Sprint 3       11 days       Mon 3/27/17       Fri 4/7/17         Fri 4/7/17       6. Testing       8 days       Mon 3/27/17       Tue 4/4/17         Mon 3/27/17       Tue 4/4/17       Mon 3/27/17       Mon 3/27/17       Mon 3/27/17         Mon 3/27/17       Tue 4/4/17       Mod 3/29/17       Mod 3/29/17       Wed 3/28/17       Wed 3/28/17       Wed 3/28/17       Wed 3/28/17       Wed 3/29/17       Wed 3/29/17       Wed 3/29/17       Wed 3/29/17       Fri 3/31/17       Sat 4/1/17       Fri 4/7/17       Mon 4/2/17       Fri 4/7/17       Mon 4/2/17       Fri 4/7/17       Mon 4/10/17       Mon 4/10/	Mode       5.4. Integration       2 days       Thu 3/16/17       Fri 3/17/17         Sprint 3       11 days       Mon 3/27/17       Fri 4/7/17         ★       6. Testing       8 days       Mon 3/27/17       Tue 4/4/17         ★       6.1. Test Analysis reports are checked       1 day       Mon 3/27/17       Mon 3/27/17         ★       6.2. Test Plans       1 day       Tue 3/28/17       Tue 3/28/17       28         ★       6.3. Integration Test       1 day       Wed 3/29/17       Wed 3/29/17       29         ★       6.4. Systems Testing       2 days       Thu 3/30/17       Fri 3/31/17       30         ★       6.5. User Acceptance Test       1 day       Sat 4/1/17       Sat 4/1/17       31         ★       7. Deployment       6 days       Sun 4/2/17       Fri 4/7/17         ★       7.1. Staging       1 day       Wed 4/5/17       Wed 4/5/17       33         Ⅲ       7.2. Preparing all documents       3 days       Thu 4/6/17       Mon 4/10/17       35




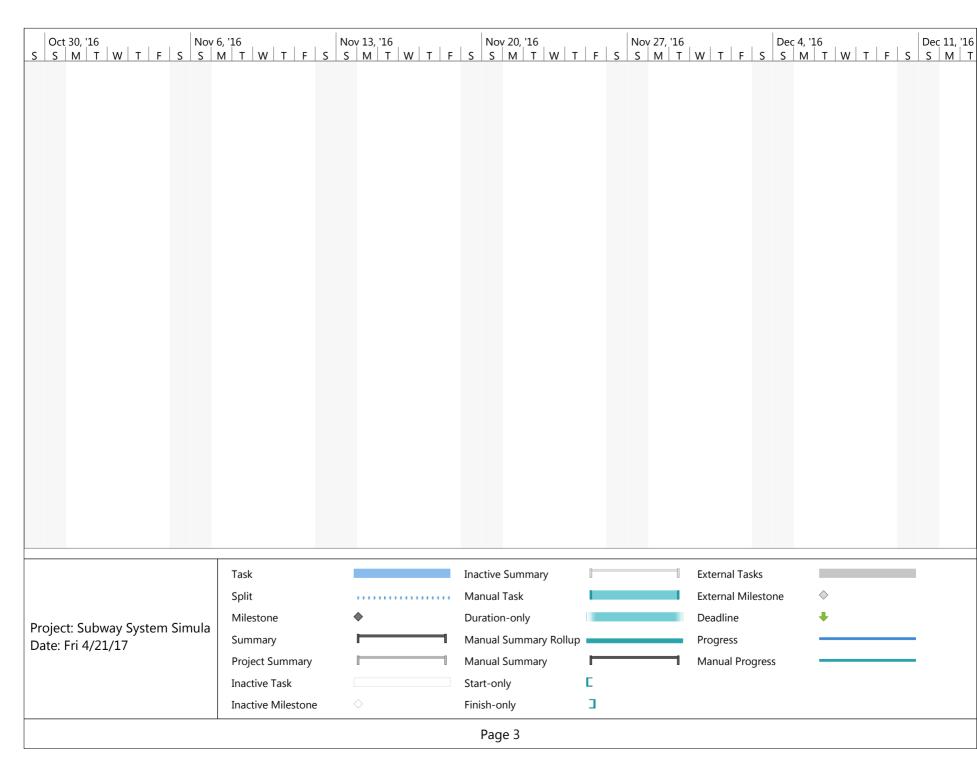


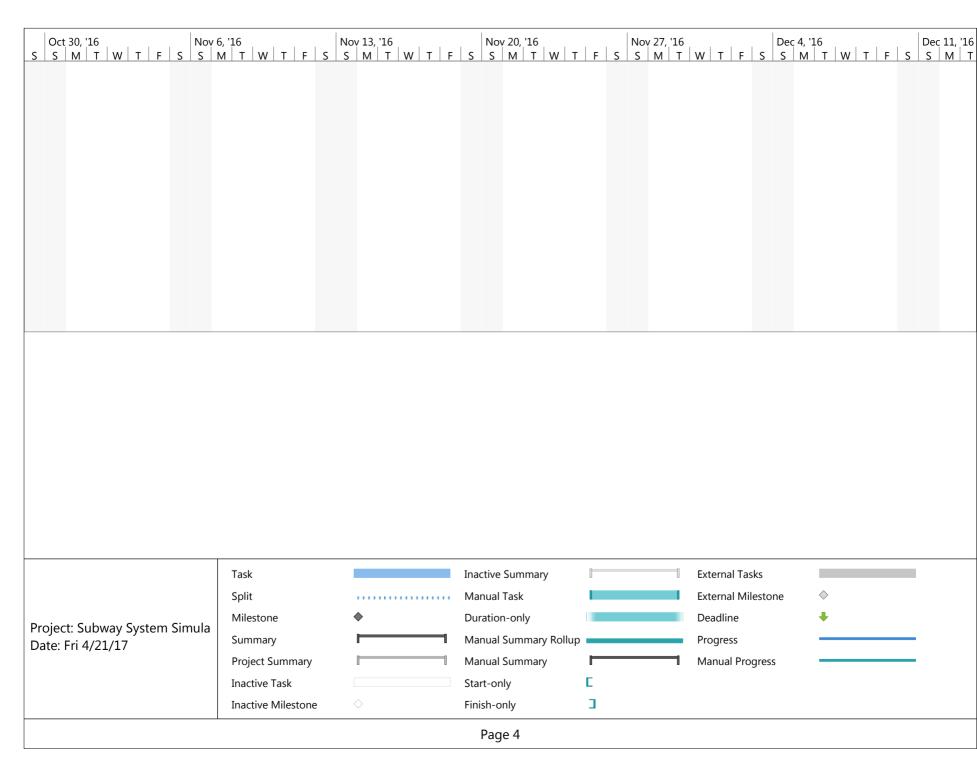


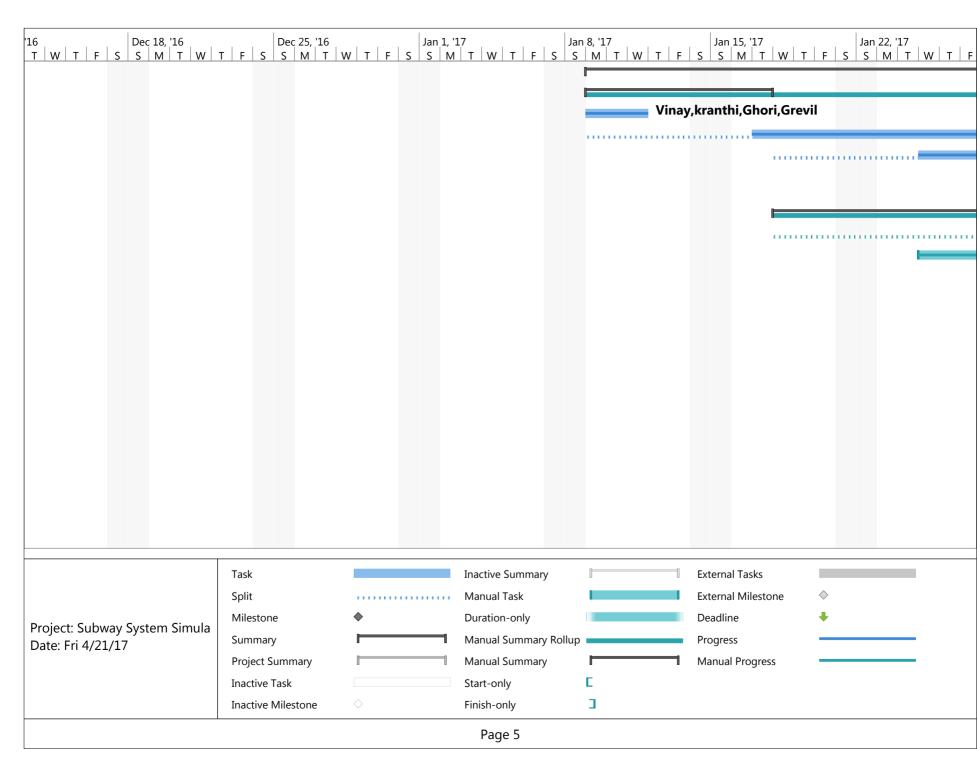


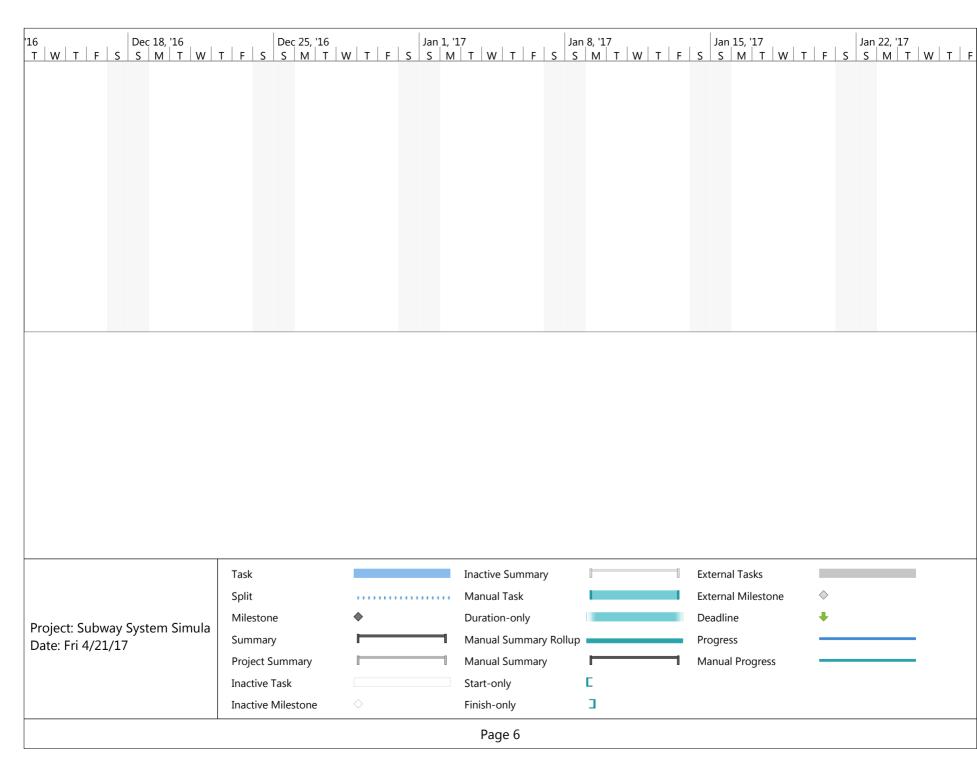

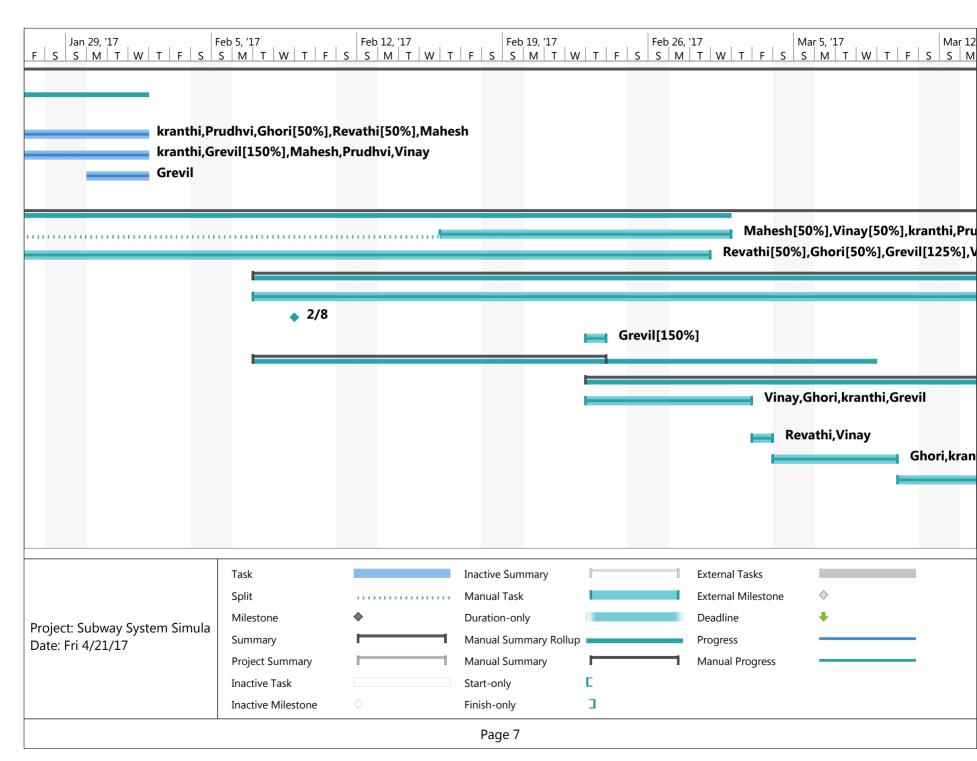

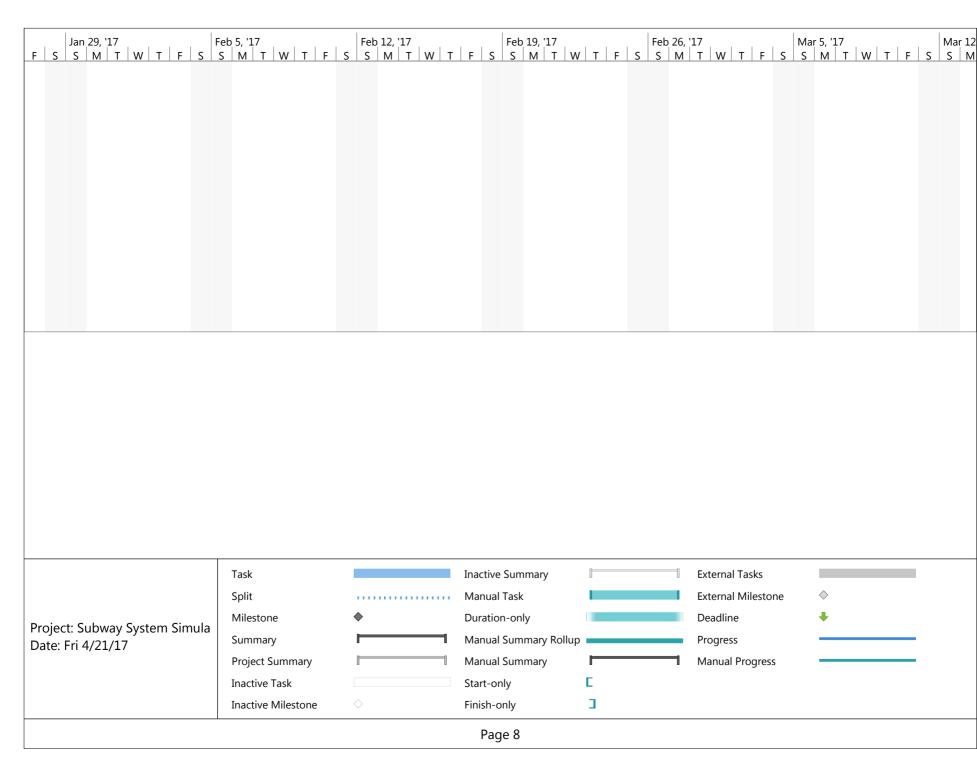

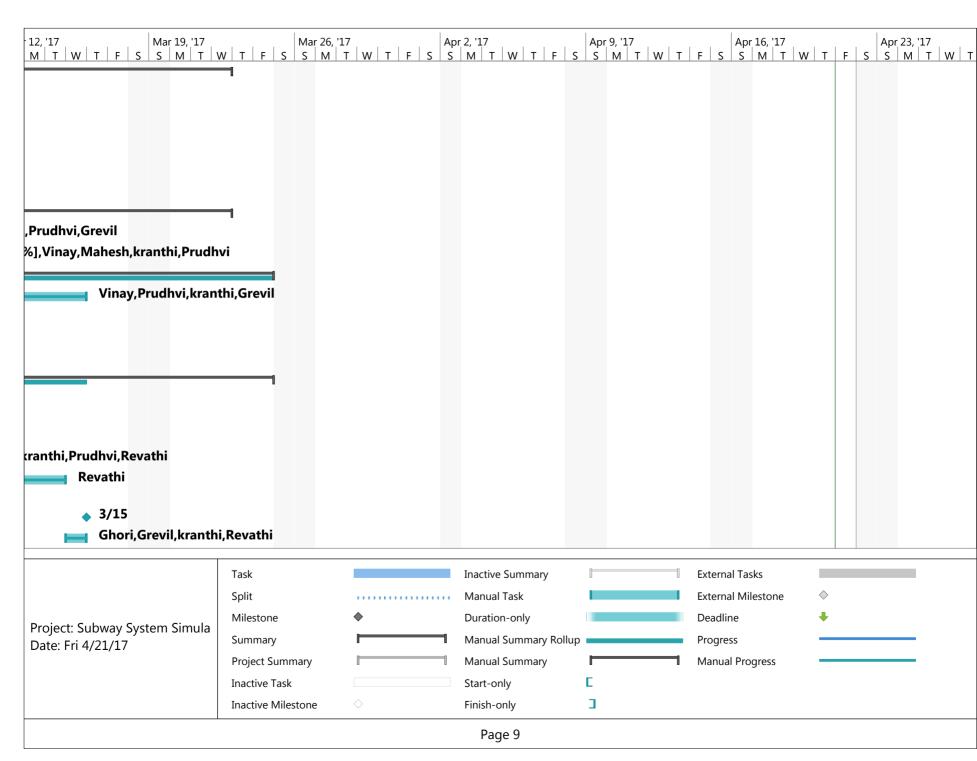

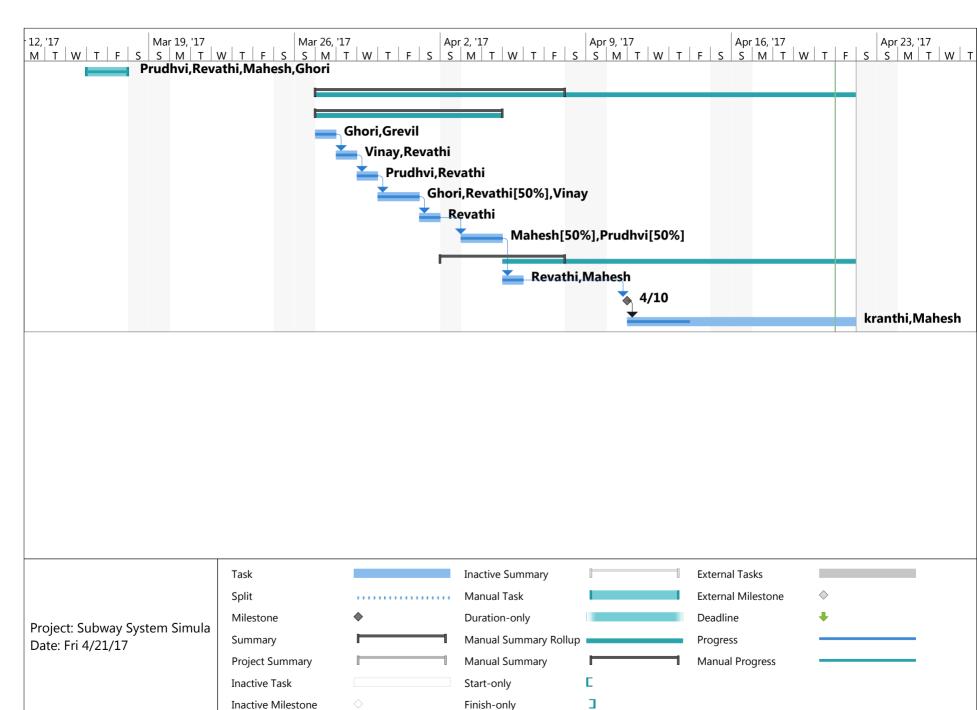

Page 10
